



		Name	Duration	Start	Finish	Actual Start	Actual Finish	Predecessors
1		Project Management & Requirements	86.625 days	8/10/26, 8:00AM	12/8/26, 2:00PM	9/14/26, 9:00AM		
2		Finalize Project Scope	1 day	8/10/26, 8:00AM	8/10/26, 5:00PM	8/10/26, 8:00AM	8/10/26, 5:00PM	
3		Finalize Requirements/constraints	1 day	8/10/26, 8:00AM	8/10/26, 5:00PM	8/10/26, 8:00AM	8/10/26, 5:00PM	
4		Deployment Bag Architecture	16 days	8/24/26, 8:00AM	9/14/26, 5:00PM		9/14/26, 5:00PM	
5	 	Complete Hardware Inventory	1 day	9/14/26, 8:00AM	9/14/26, 5:00PM	9/14/26, 8:00AM	9/14/26, 5:00PM	
6	 	Define Canonical Student Bag	3 days	8/24/26, 8:00AM	8/26/26, 5:00PM	8/24/26, 8:00AM	8/26/26, 5:00PM	2;3
7	 	Define Management/infrastructure Bag	3 days	8/27/26, 8:00AM	8/31/26, 5:00PM	8/27/26, 8:00AM	8/31/26, 5:00PM	2;3
8	 	Finalize Physical Topology	0.25 days	9/1/26, 8:00AM	9/1/26, 10:00AM	9/1/26, 8:00AM	9/1/26, 10:00AM	6;7
9	 	Architecture Review	4 days	9/7/26, 8:00AM	9/10/26, 5:00PM	9/7/26, 8:00AM	9/10/26, 5:00PM	
10		Prototype & Validation	19.083 days	9/14/26, 8:00AM	10/9/26, 8:39AM	9/14/26, 9:00AM		
11	 	Assemble Prototype Bag	0.125 days	9/14/26, 8:00AM	9/14/26, 9:00AM	9/14/26, 8:00AM	9/14/26, 9:00AM	9
12		Establish Baseline Configurations	5 days	9/14/26, 9:00AM	9/21/26, 9:00AM	9/14/26, 9:00AM		11
13		Develop Reset Procedure	5 days	9/28/26, 8:00AM	10/2/26, 5:00PM			12
14		Validate Production Isolation	0.042 days	10/1/26, 8:00AM	10/1/26, 8:20AM			12
15		Test Representative Topology	0.125 days	10/5/26, 8:00AM	10/5/26, 9:00AM			13;14
16		Pilot Architecture Approved	0.083 days	10/9/26, 8:00AM	10/9/26, 8:39AM			15
17		Lab Development & Delivery	42.542 days	10/9/26, 8:39AM	12/8/26, 2:00PM			
18		Lab 1	8.25 days	10/9/26, 8:39AM	10/21/26, 10:39AM			
19		Lab 1 Design	2 days	10/9/26, 8:39AM	10/13/26, 8:39AM			16
20		Lab 1 Implementation	5 days	10/13/26, 8:39AM	10/20/26, 8:39AM			19
21		Lab 1 Independent Validation / Pilot	0.125 days	10/20/26, 8:39AM	10/20/26, 9:39AM			20
22		Lab 1 Revision & Approval	0.125 days	10/20/26, 9:39AM	10/20/26, 10:39AM			21
23		Lab 1 Due	1 day	10/20/26, 10:39AM	10/21/26, 10:39AM			22
24		Lab 2	8.917 days	10/20/26, 8:39AM	10/30/26, 5:00PM			
25		Lab 2 Design	2 days	10/20/26, 8:39AM	10/22/26, 8:39AM			20
26		Lab 2 Implementation	5 days	10/22/26, 8:39AM	10/29/26, 8:39AM			25
27		Lab 2 Independent Validation / Pilot	0.125 days	10/29/26, 8:39AM	10/29/26, 9:39AM			26
28		Lab 2 Revision & Approval	0.125 days	10/29/26, 9:39AM	10/29/26, 10:39AM			27
29		Lab 2 Due	1 day	10/30/26, 8:00AM	10/30/26, 5:00PM			28
30		Lab 3	8.25 days	10/29/26, 8:39AM	11/10/26, 10:39AM			
31		Lab 3 Design	2 days	10/29/26, 8:39AM	11/2/26, 8:39AM			26
32		Lab 3 Implementation	5 days	11/2/26, 8:39AM	11/9/26, 8:39AM			31
33		Lab 3 Independent Validation / Pilot	0.125 days	11/9/26, 8:39AM	11/9/26, 9:39AM			32
34		Lab 3 Revision & Approval	0.125 days	11/9/26, 9:39AM	11/9/26, 10:39AM			33

Resource Names	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton;Navya Gupta;Grayson Glass	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton;Navya Gupta;Grayson Glass	
Tyler Dalton;Navya Gupta;Grayson Glass	
Tyler Dalton;Navya Gupta;Grayson Glass	
Tyler Dalton;Navya Gupta	
Tyler Dalton;Jason Gerst;Emrah Ugurlu	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton	
Navya Gupta;Grayson Glass	
Navya Gupta;Grayson Glass	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton	
Navya Gupta;Grayson Glass	
Navya Gupta;Grayson Glass	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	
Tyler Dalton	
Navya Gupta;Grayson Glass	
Navya Gupta;Grayson Glass	
Tyler Dalton;Navya Gupta;Emrah Ugurlu	

		Name	Duration	Start	Finish	Actual Start	Actual Finish	Predecessors
35		Lab 3 Due	1 day	11/9/26, 10:39AM	11/10/26, 10:39AM			34
36		Lab 4	9.917 days	11/9/26, 8:39AM	11/20/26, 5:00PM			
37		Lab 4 Design	2 days	11/9/26, 8:39AM	11/11/26, 8:39AM			32
38		Lab 4 Implementation	5 days	11/11/26, 8:39AM	11/18/26, 8:39AM			37
39		Lab 4 Independent Validation / Pilot	0.125 days	11/18/26, 8:39AM	11/18/26, 9:39AM			38
40		Lab 4 Revision & Approval	0.125 days	11/18/26, 9:39AM	11/18/26, 10:39AM			39
41		Lab 4 Due	1 day	11/20/26, 8:00AM	11/20/26, 5:00PM			40
42		Deployment & Scaling	33 days	10/12/26, 8:00AM	11/25/26, 5:00PM			
43		Determine Production Quantity	2 days	10/12/26, 8:00AM	10/13/26, 5:00PM			9
44		Finalize BOM	1 day	10/14/26, 8:00AM	10/14/26, 5:00PM			43
45		Procurement Approval	0.042 days	10/20/26, 8:00AM	10/20/26, 8:20AM			44
46		Procure Core SBC Kits	7 days	10/20/26, 8:20AM	10/29/26, 8:20AM			45
47		Procure NVMe Upgrades	7 days	10/20/26, 8:20AM	10/29/26, 8:20AM			45
48		Procure Network Adapters	7 days	10/20/26, 8:20AM	10/29/26, 8:20AM			45
49		Procure Troubleshooting Stations	7 days	10/20/26, 8:20AM	10/29/26, 8:20AM			45
50		Procure SBC HA Spares	7 days	10/20/26, 8:20AM	10/29/26, 8:20AM			45
51		Receive & Inspect Equipment	0.25 days	10/29/26, 8:20AM	10/29/26, 10:20AM			46;47;48;49;50
52		Asset Tag / Inventory Equipment	0.25 days	10/29/26, 10:20AM	10/29/26, 1:20PM			51
53		Assemble Deployment Bags	5 days	11/6/26, 8:00AM	11/12/26, 5:00PM			52
54		Configure Standardized Baselines	7 days	11/13/26, 8:00AM	11/23/26, 5:00PM			53
55		Validate Bags Against Standard	2 days	11/24/26, 8:00AM	11/25/26, 5:00PM			54
56		Operational Documentation	25 days	10/27/26, 8:00AM	11/30/26, 5:00PM			
57		Student Deployment Instructions	1 day	11/26/26, 8:00AM	11/26/26, 5:00PM			55
58		Instructor/TA Deployment Guide	1 day	11/26/26, 8:00AM	11/26/26, 5:00PM			55
59		Reset/recovery runbook	1 day	11/27/26, 8:00AM	11/27/26, 5:00PM			55;57;58
60		Hardware Inventory Documentation	0.5 days	10/27/26, 8:00AM	10/27/26, 1:00PM			
61		Laminated Bag Inventory Sheet	0.5 days	10/27/26, 1:00PM	10/27/26, 5:00PM			60
62		Topology Documentation	0.75 days	11/24/26, 8:00AM	11/24/26, 3:00PM			60
63		Troubleshooting Documentation	1 day	11/30/26, 8:00AM	11/30/26, 5:00PM			57;58;59
64		Final Validation & Handoff	5.625 days	12/1/26, 8:00AM	12/8/26, 2:00PM			
65		End-to-end Regression Testing	3 days	12/1/26, 8:00AM	12/3/26, 5:00PM			63
66		Documentation Review	1 day	12/4/26, 8:00AM	12/4/26, 5:00PM			63;65
67		Instructor/TA Operational Walkthrough	0.125 days	12/7/26, 8:00AM	12/7/26, 9:00AM			66
68		Resolve Final Dependencies	1 day	12/7/26, 9:00AM	12/8/26, 9:00AM			67

Resource Names
Tyler Dalton
Navya Gupta;Grayson Glass
Navya Gupta;Grayson Glass
Tyler Dalton;Navya Gupta;Emrah Ugurlu
Tyler Dalton;Emrah Ugurlu
Tyler Dalton;Emrah Ugurlu
Tyler Dalton;Emrah Ugurlu;Jason Gerst
Tyler Dalton;Jason Gerst;Emrah Ugurlu;Raspberry Pi 5 CanaKit[20 kits]
Tyler Dalton;Jason Gerst;Emrah Ugurlu;NVMe Storage Upgrade[20 units]
Tyler Dalton;Jason Gerst;Emrah Ugurlu;USB GbE Adapter[20 adapters]
Jason Gerst;Tyler Dalton;Emrah Ugurlu;Troubleshooting Stations[2 stations]
Tyler Dalton;Emrah Ugurlu;Jason Gerst;HA Spares[2 units]
Tyler Dalton
Navya Gupta;Grayson Glass;Tyler Dalton
Tyler Dalton;Navya Gupta;Grayson Glass
Navya Gupta;Grayson Glass
Tyler Dalton
Navya Gupta;Grayson Glass
Navya Gupta;Grayson Glass
Navya Gupta;Grayson Glass
Tyler Dalton
Tyler Dalton
Tyler Dalton
Navya Gupta;Grayson Glass
Tyler Dalton;Navya Gupta;Grayson Glass;Emrah Ugurlu
Tyler Dalton;Navya Gupta;Emrah Ugurlu
Tyler Dalton;Navya Gupta;Grayson Glass;Emrah Ugurlu
Tyler Dalton;Navya Gupta



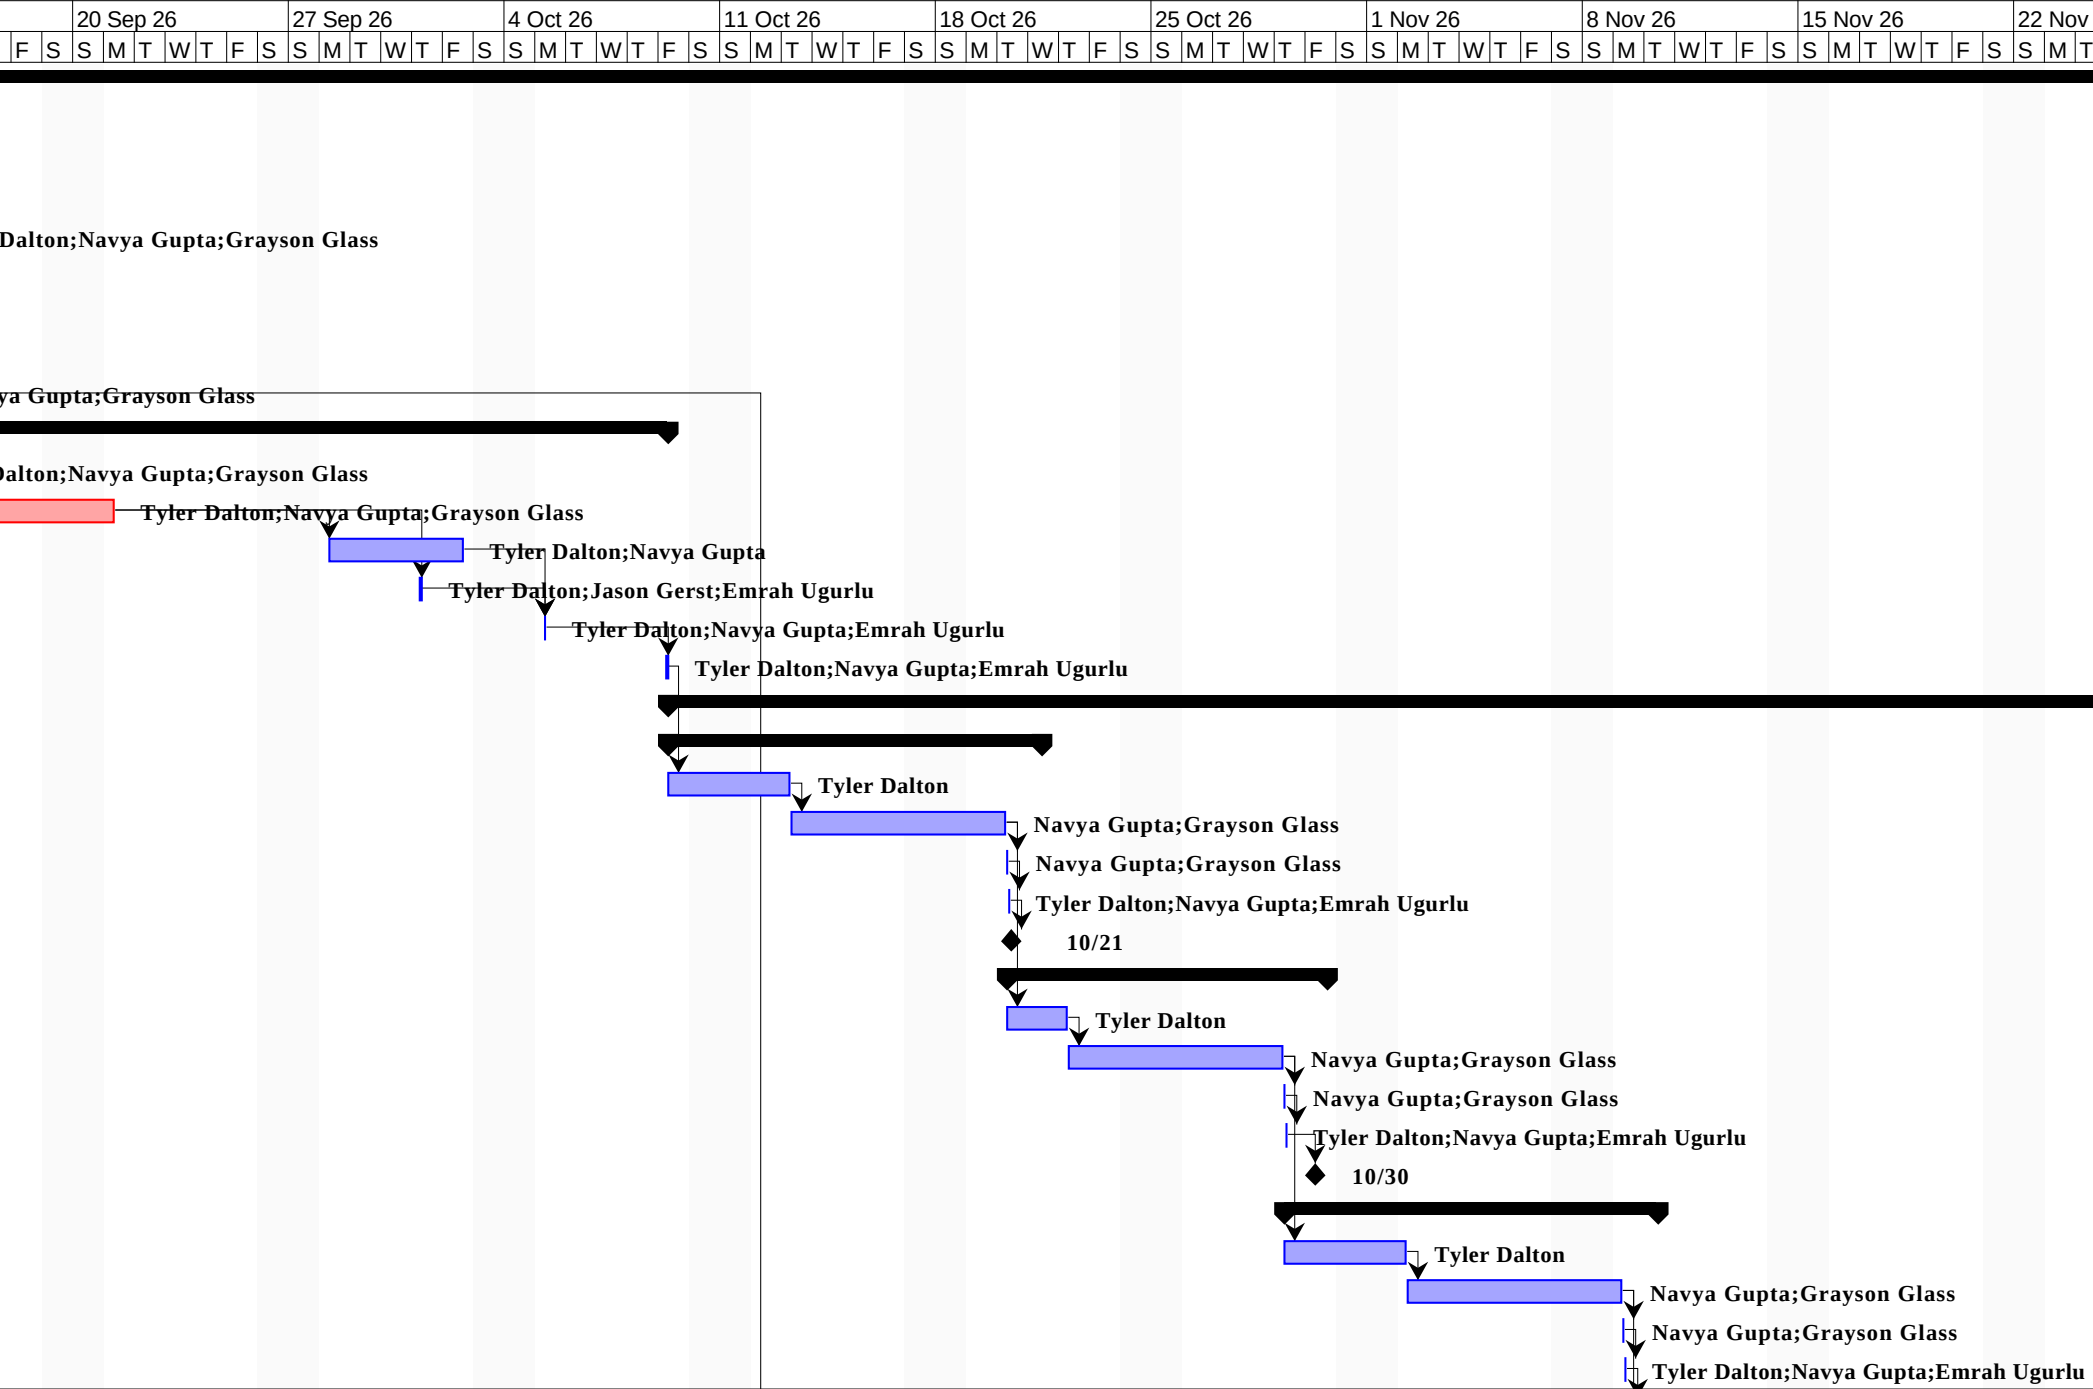

The Gantt chart displays the deployment schedule for the 'deployment-bags-libre' project. The timeline starts on November 26, 2026, and ends on January 3, 2027. The chart is organized into weekly blocks, with days of the week (W, T, F, S) indicated for each week. A thick black bar at the top indicates the overall deployment period from November 26 to December 1, 2026. The chart shows the following deployment tasks and their durations:

- Grayson Glass** (Red bar): Deployed on November 26, 2026.
- Grayson Glass** (Red bar): Deployed on November 27, 2026.
- Navya Gupta; Grayson Glass** (Red bar): Deployed on November 28, 2026.
- Grayson Glass** (Red bar): Deployed on November 29, 2026.
- Grayson Glass** (Red bar): Deployed on November 30, 2026.
- Grayson Glass** (Red bar): Deployed on December 1, 2026.
- Grayson Glass** (Red bar): Deployed on December 2, 2026.
- Grayson Glass** (Red bar): Deployed on December 3, 2026.
- Grayson Glass** (Red bar): Deployed on December 4, 2026.
- Grayson Glass** (Red bar): Deployed on December 5, 2026.
- Grayson Glass** (Red bar): Deployed on December 6, 2026.
- Grayson Glass** (Red bar): Deployed on December 7, 2026.
- Grayson Glass** (Red bar): Deployed on December 8, 2026.
- Grayson Glass** (Red bar): Deployed on December 9, 2026.
- Grayson Glass** (Red bar): Deployed on December 10, 2026.
- Grayson Glass** (Red bar): Deployed on December 11, 2026.
- Grayson Glass** (Red bar): Deployed on December 12, 2026.
- Grayson Glass** (Red bar): Deployed on December 13, 2026.
- Grayson Glass** (Red bar): Deployed on December 14, 2026.
- Grayson Glass** (Red bar): Deployed on December 15, 2026.
- Grayson Glass** (Red bar): Deployed on December 16, 2026.
- Grayson Glass** (Red bar): Deployed on December 17, 2026.
- Grayson Glass** (Red bar): Deployed on December 18, 2026.
- Grayson Glass** (Red bar): Deployed on December 19, 2026.
- Grayson Glass** (Red bar): Deployed on December 20, 2026.
- Grayson Glass** (Red bar): Deployed on December 21, 2026.
- Grayson Glass** (Red bar): Deployed on December 22, 2026.
- Grayson Glass** (Red bar): Deployed on December 23, 2026.
- Grayson Glass** (Red bar): Deployed on December 24, 2026.
- Grayson Glass** (Red bar): Deployed on December 25, 2026.
- Grayson Glass** (Red bar): Deployed on December 26, 2026.
- Grayson Glass** (Red bar): Deployed on December 27, 2026.
- Grayson Glass** (Red bar): Deployed on December 28, 2026.
- Grayson Glass** (Red bar): Deployed on December 29, 2026.
- Grayson Glass** (Red bar): Deployed on December 30, 2026.
- Grayson Glass** (Red bar): Deployed on December 31, 2026.
- Grayson Glass** (Red bar): Deployed on January 1, 2027.
- Grayson Glass** (Red bar): Deployed on January 2, 2027.
- Grayson Glass** (Red bar): Deployed on January 3, 2027.

		Name	Duration	Start	Finish	Actual Start	Actual Finish	Predecessors
69		Project Handoff / Semester Completion	0.5 days	12/8/26, 9:00AM	12/8/26, 2:00PM			68

--	--	--	--	--	--	--	--	--
